

Rodney A. Cook Director

| December 19, 2024 | BCC Agenda Date/Item: |
|-------------------|-----------------------|
| | |

Board of County Commissioners Clackamas County

Approval of Change Order to a Public Improvement Contract with ASA Construction for the Clackamas Village Project. Change Order Value is \$362,085.66 for 4 months. Total Contract Value is increased to \$3,700,627.22 for 1 year. Funding is through Supportive Housing Services Measure Funds. No County General Funds are involved.

| Previous Board | September 20, 2023 – Board approved Supportive Housing Services spend | | | |
|----------------|---|---|-------------------------------|--|
| Action/Review | down plan, including funding for Clackamas Village construction | | | |
| | November 22, 2023 – Boa | November 22, 2023 – Board approved acquisition of site from the Development | | |
| | Agency | | | |
| | December 13, 2023 – Boa | ard approved construction | n and operations funding plan | |
| | and request to proceed with construction and operations solicitations | | | |
| | April 25, 2024 – Board approved construction contract with ASA Construction | | | |
| | July 20, 2024 – Department approved Change Order #1 | | | |
| | August 21, 2024 – Department approved Change Order #2 | | | |
| | December 17, 2024 – Cha | ange Order #3 briefed at | Issues | |
| Performance | This funding aligns with th | ne County's strategic prior | rity to ensure safe, | |
| Clackamas | healthy and secure communities. | | | |
| Counsel Review | NA | Procurement Review | Yes | |
| Contact Person | Mark Sirois | Contact Phone | 503-351-7240 | |

EXECUTIVE SUMMARY: The Housing & Community Development Division of the Health, Housing & Human Services Department is requesting approval of Change Order #3 to the construction contract with ASA Construction for Clackamas Village. Change Order #3 adds #362,085.66 to cover costs associated with code requirements and unforeseen site conditions.

Clackamas County is developing a new transitional housing village at the site adjacent to the County's Veterans Village. The new site, Clackamas Village, will provide people experiencing homelessness with safety off the streets and supportive services to aid in their transition to safe and stable permanent housing. The site's 13 modular building structures will include a kitchen module, two office modules, two bathroom modules, and eight three-bedroom sleeping modules, with a total of 24 housing units.

ASA Construction, a Clackamas County-based company, was the lowest responsive bidder of the three bid proposals submitted for consideration in March 2024. The construction contract with ASA Construction was executed in April 2024, and construction started in July 2024.

For Filing Use Only

During construction, a number of changes have been required. This includes changes made at the request of the County, those required for code, and those that were needed to address unforeseen site conditions. Change Orders #1 and #2 added additional neighbor fencing, tree removals, tree hedges along the new fence, parking lot lights, an emergency generator connection for use during severe weather events, and temporary security cameras for site security during construction. Change Orders #1 and #2 were executed by the department since the changes were less than 20% of the construction contract amount and less than \$150,000 in total cost.

Change Order #3 includes modifications to meet fire and safety code requirements for a much longer driveway and turnaround to accommodate fire trucks. The extensive re-design of the driveway, landscaping, and rain gardens is to accommodate more surface area created by a larger driveway and turnaround. In addition, Change Order #3 covers costs related to the unforeseen site conditions of significant amounts of river rock covering the site's surface. Additional work was needed to remove river rock to create level and structurally sound buildable areas. The code requirements and unforeseen site conditions resulted in additional work and materials for buried trash removal, soil removal, infill, driveway base, additional foundation and landscaping work, concrete, and pavement.

| | County Requested: | | Required by Code: | | Unforeseen Site Conditions: | | С | hange Order Totals: |
|----------------|----------------------|------------|-------------------|------------|-----------------------------------|-----------|----|------------------------|
| Change Order 1 | \$ | 72,246.39 | | | \$ | 6,045.28 | \$ | 78,291.67 |
| Change Order 2 | \$ | 48,744.14 | | | | | \$ | 48,744.14 |
| Change Order 3 | \$ | 74,868.79 | \$ | 199,870.22 | \$ | 87,346.65 | \$ | 362,085.66 |
| Totals | \$ | 195,859.32 | \$ | 199,870.22 | \$ | 93,391.93 | \$ | 489,121.47 |

 Original Contract Amount:
 \$3,211,505.75

 Change Orders:
 \$489,121.47 (15%)

 New Contract Amount:
 \$3,700,627.22

The project is scheduled for completion and opening in Spring 2025.

RECOMMENDATION: Staff respectfully recommends that the Board of County Commissioners approve Change Order #3 and authorize Chair Smith or her designee to sign on behalf of Clackamas County.

Respectfully submitted,

Rodney A. Cook

Rodney A. Cook


Director of Health, Housing and Human Services

CHANGE ORDER COVER FORM

| ASA Construction, LLC | () Contractor |
|--|--|
| 19100 S. Hwy 99E | () Project Manager |
| Oregon City, OR 97045 | () H3S Admin/ BCC |
| Proj. Name: New Clackamas Transitional Housing Village Project | |
| Proj. Address: 16575 SE 115 th Avenue | Contract Date: 4/25/2024 |
| Clackamas, OR 97015 | Change Order Date: 11/14/2024 Notice to Proceed: 7/9/2024 |
| To: Clackamas County Health, Housing and Human Services Dept. Public Services Building | |
| 2051 Kaen Road, 2 nd Floor | |
| Oregon City, Oregon 97045 | |
| The following changes have been authorized by Clackamas County design/architecture, LLC. See the listed change(s) to the project an construction contract: Change Order #3 items are as follows: 1) AEC Erosion Control (Sub.)/ expanded Rain Gardens, Trees add 2) Toby Davis Concrete (Sub.)/ Trash Pad, Fire Lane Pad, Bollards 3) Pacific Mobile Structures (Sub.)/ add of 2 office doors to the mat 4) Epling Electrical (Sub.)/ 2 pathway bollard light fixtures | ed,1yr. Maint\$ 36,250.00, more rebar work\$ 11,866.50 in structure\$ 22,866.00\$ 2,639.90 or fire safety, exc\$194,423.44\$ 16,545.92\$ 77,493.90 |
| Attached is the supporting documentation from ASA Construct | ion for this Change Order. |
| Original Contact Price | |
| Net Change by Previous Change Orders (#1 & #2) | |
| Contract Price prior to this Change Order | \$3,338,541.57 |
| Contract Price will be (increased) (unchanged) by this Change Order | |
| The new Contract Price including this Change Order will be | \$3,700,627.23 |
| The Contract Time will be increased by this Change Order (48) cal | • |
| Date is (180 days)February 24, 2025), and original Final Completion | |
| Contract End Date for paperwork close-out and retainage release is | (240 days April 21, 2025). |

[Signature page to follow]

| Approved: | | Approved: | |
|--|----------------------|-----------|------------------|
| by: Heather ASA, CEO ASA Construction, LLC | 11/20/2024 (date) | by: | /21/24 (date) |
| Approved: | | Approved: | |
| by: Mark Sirois Mark Sirois, HCDD Manager Clack. Cty. HCDD | 11-21-24 (date) | by: | (date) |

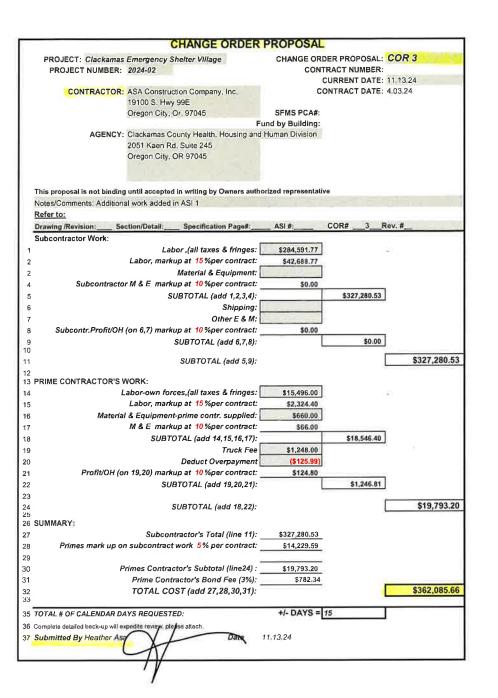

PACIFIC MOBILE STRUCTURES, INC.



Project Change Order Breakdown Summary

Date 09/16/24

Clackamas Village PMSI PCO # 1.0

Add Building Scope - Office #1 & #2

| Description of Change: | Qty. | | Cost | |
|--|------|----|----------|----------------|
| Blazer - Office #1: | | _ | | |
| - Resubmittal, drafting and general office work | 1.00 | \$ | 441.00 | \$ 441.00 |
| - Add (1) Interior door with passage lock - office to office - same as "door #3" | 1.00 | \$ | 1,221.00 | \$ 1,221.00 |
| - Paint (1) Accent wall | 1.00 | \$ | 378.00 | \$ 378.00 |
| Blazer - Office #2: | | | | |
| - Resubmittal, drafting and general office work | 1.00 | \$ | 441.00 | \$ 441.00 |
| - Add (1) Interior door with passage lock - office to office - same as "door #3" | 1.00 | \$ | 1,221.00 | \$ 1,221.00 |
| - Paint (1) Accent wall | 1.00 | \$ | 378.00 | \$ 378.00 |
| PMSI - Superintendent | 2.00 | \$ | 85.00 | \$ 170.00 |

| 4,250.00 | \$ | | SUBTOTAL |
|----------|----|--------|-------------------|
| 425.00 | \$ | 10.00% | PROFIT & OVERHEAD |
| 95.41 | \$ | 2% | BOND |
| 4.770.41 | Ś | | TOTAL |

PACIFIC MOBILE STRUCTURES, INC.



Project Change Order Breakdown Summary

Date 10/31/24

Clackamas Village

PMSI PCO # 2.0

Add (26) Access Panels to Sleeping Units #1-8 and RR Units #1-2

| Description of Change: | Qty. | Cost | |
|---|-------|-----------------|-----------|
| Blazer - Sleeping Units #1-8 - Add (24) 18" x 24" Floor | | | |
| Access Panels | 24.00 | \$ 716.00 \$ | 17,184.00 |
| Blazer - RR Units #1-2 - Add (2) 18" x 24" Floor Access | | | |
| Panels | 2.00 | \$ 716.00 \$ | 1,432.00 |

| 18,616.00 | \$ | SUBTOTAL |
|-----------|--------------|-------------------|
| 1,861.60 | \$ 10.00% | PROFIT & OVERHEAD |
| 417.91 | \$ 2% | BOND |
| 20,895.51 | \$ | TOTAL |



Change Order CCB # 209696

P.O. Box 755 Molalla, OR 97038

Change order :3

Prepared by: Kevin Beede 503-701-6353

Attention: Heather Asa

Project Name: Clackamas Emergency Shelter

| NOTES | |
|---------------------------------------|-----------|
| | |
| | |
| ITEMIZED ESTIMATE: TIME AND MATERIALS | AMOUNT |
| | 04 400 00 |

| ITEMIZED ESTIMATE: TIME AND MATERIALS | AMOUNT |
|--|------------|
| Fire lane and parking lot includes excavating, 8" of rock, compacting, and grading estimated 252 tons @ \$85 | 21,433.00 |
| Excavation for road and gps work. 154 yards of dirt @ \$55 a yard | 8,500.00 |
| 6" storm, 15' 95 plus all fitting roughly \$3750 | 6,525.00 |
| 3 catch basins \$2,500 each | 7,500.00 |
| Extra drain rock and rip rap and pond excavating. 2283 additional sqft. @14.45 a sqft. | 33,007.79 |
| Gravel pad 1/4" minus at 2" thick. Area increased by1238 sqft @ \$4.03 sqft. | 5,000.00 |
| Swale ditch only no soil or rock. 435 LF swale @ \$34.98 LF | 15,225.00 |
| Deduction from original bid work no longer being done in rock pathway and round about. All materials to be left on site | (6,789.00) |
| 2" of Bark nuggets in all landscaping areas at 2" thick. Area is 20,899 Sqft. @ \$1.25 sqft. | 16,675.00 |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| TOTAL ESTIMATED COST | 107,076.79 |

By signing this change order you are approving and requesting the changes or additions to the original scope of work and understand that this constitutes as a change order. It will be billed in addition to original bid work unless otherwise specified.

| Kevin Beede | n | August 12 2024 |
|-------------|---|----------------|
| | | |



Change Order CCB # 209696

P.O. Box 755 Molalla, OR 97038

Change order 14

TOTAL ESTIMATED COST

16,133.65

Attention: Heather Asa

Project Name: Clackamas Emergency Shelter

| NOTES | |
|--|------------------|
| | |
| ITEMIZED ESTIMATE: TIME AND MATERIALS | AMOUNT |
| \$85 a ton for for rock and compaction to bring it up to grade 79.49 ton of rock | 6,756.65 |
| \$55 a yard to dig it up and haul it off 50 yards of material | 2,750.00 |
| Dumping fees are \$165 a ton plus a \$27 transaction fee per load 40 ton | 6,627.00 |
| | 9 7 . |
| | 0.E |
| | 75 Yes |
| | 12 A |
| | |

By signing this change order you are approving and requesting the changes or additions to the original scope of work and understand that this constitutes as a change order. It will be billed in addition to original bid work unless otherwise specified.

| Kevin Beede | August 27 2024 |
|-------------|----------------|
| Signature | DATE |



Change Order CCB # 209696

P.O. Box 755 Molalla, OR 97038

Change order:6

| Prepared by: Kevin | Beede 503-701-6353 |
|---------------------------|--------------------|
| Attention: Heather | Asa |

Project Name: Clackamas Emergency Shelter

| ITEMIZED ESTIMATE: TIME AND MATERIALS | AMOUNT |
|--|-----------|
| Over excavate 275 yards at \$55 a yard. Includes digging, moving dirt, backfilling, labor, and the additional erosion control for winter conditions. There is no haul off accounted for. Everything to stay on site. | 15,125.00 |
| TOTAL ESTIMATED COST | 15,125.00 |

NOTES

By signing this change order you are approving and requesting the changes or additions to the original scope of work and understand that this constitutes as a change order. It will be billed in addition to original bid work unless otherwise specified.

| Kevin Beede | September 9, 2024 |
|-------------|-------------------|
| Signature | DATE |



Prepared by: Kevin Beede 503-701-6353

Project Name: Clackamas Emergency Shelter

Kevin Beede Signature

Attention: Heather Asa

Change Order # 209696

O. Box 755 lla, OR 97038

Change order 17

October 25, 2024

DATE

| CCB # |
|-------|
| P.0 |
| Mola |
| |

| ITEMIZED ESTIMATE: TIME AND MATERIALS | | AMOUNT |
|---|----------------------|------------------------|
| Removal of 1600 yards of soil and installing a haul road for access,includes rock Excavate building pads and installing 4" of compacted rock (110 cy of rock) | | 38,603.00 17,485.00 |
| | | |
| | | |
| | TOTAL ESTIMATED COST | 56,088.00 |

By signing this change order you are approving and requesting the changes or additions to the original scope of work and understand that this constitutes as a change order. It will be billed in addition to original bid work unless otherwise specified.

NOTES



Change Order

Epling Electric
Printed: Sep 25, 2024

1295 SE 62nd Ave, Hillsboro, OR 97123-2968

Phone: 9712362175

Owner Info None

Job Info 16590 SE 115th Ave Clackamas, OR 97015 Change Order ID
0003

ASA - Clackamas Village Project

| COID | Created / Approved Date | | Price |
|------|-------------------------|-------------|------------|
| 0003 | Created: Pending | Aug 9, 2024 | \$2,639.90 |

Description

ASI 1 (additional bollard lights)

CCB#238584

COBID Certified: ESB #13511 Proposal Type: Hard Bid Prevailing Wage: Yes

Scope of Work:

-Provide and install (2) pathway bollard light fixtures

*This CO is in response to ASI 1

Exclusions and Clarifications:

- · All work to be performed during normal business hours (Monday-Friday, 7am-3pm)
- · Excludes sheetrock patching and painting if needed
- · Excludes conduit painting
- Excludes all low voltage (fire alarm, access control, security, network, HVAC, etc) unless otherwise noted
- · Excludes core drilling, concrete saw cutting & patching
- · Excludes roof penetrations
- Excludes removal/off-site disposal of demo materials unless otherwise noted
- · Excludes unforeseen or hidden conditions/issues
- Does not cover or account for hazardous locations unless specifically noted
- · Does not include plan review unless specifically noted

| Items | Cost Types | Description | Qty / Unit | Unit Price | Price |
|---|------------|-------------|------------|------------|----------|
| Apprentice Prevailing Wage 1010-Labor | | | 4 each | \$138.00 | \$552.00 |
| Journeyman Prevailing Wage | | | 4 Each | \$168.00 | \$672.00 |

Change Order Print

| Items | Cost Types | Description | Qty / Unit | Unit Price | Price |
|---------------------------------------|------------|---------------------|------------|------------|------------|
| 1010-Labor | | | | | |
| #10 THHN 3010-Material | | (3) conductors | 120 each | \$0.40 | \$48.36 |
| 3/4 PVC 90 3010-Material | | | 4 each | \$5.42 | \$21.68 |
| 3/4 PVC Coupling 3010-Material | | | 8 each | \$0.60 | \$4.78 |
| 3/4 PVC, Schedule 40 3010-Material | | | 40 each | \$1.03 | \$41.08 |
| Lighting Quote 3010-Material | | budget (2 bollards) | 2 each | \$650.00 | \$1,300.00 |

| Status | Signature | Date |
|--------------|-----------|------|
| Approved by: | | |

| Approval Comments |
|-------------------|
| |

I confirm that my action here represents my electronic signature and is binding.

TOTAL AMOUNT OF CHANGE ORDER:

\$2,639.90



EASTSIDE PAVING, INC.

PO BOX 1049 GRESHAM, OR 97030 Ph#: 503 492-7563 fax#: 503 492-7564 CCB# 068962 WA# EASTSPI087K1 sean@eastsidepaving.com

| D | Contra | -4 |
|-------|---------|-------|
| Prime | • Antra | ırtar |

May 13, 2024

Clackamas Village ASI 1 CO#1 Clackamas, Or.

Additional parking lot paving per ASI#1 Drawings

Note: This proposal may be withdrawn if not accepted within 30 days.

4016 Sq. Ft. @ \$4.12 Per----\$16545.92

1 Mobilization included in price. Any additional to be billed at \$3000.00 EA.

Price based off current Plant Pricing.

Price based off current ODOT Asphalt Oil Index price of \$573.00 at time of bid.

Exclusions: Traffic control, testing, permits, fees, sales tax, grind, saw cut, fine grading, pavement marking, nights, weekends, any drainage less than 2%.

I Propose hereby to furnish material and labor – complete in accordance with above specifications.

All material is guaranteed to be as specified. All work to be completed in a workmanlike manner according to standard practices. Payment to be made upon completion unless otherwise agreed. Access will be agreed upon by the owner to hold Eastside Paving, Inc. absolutely harmless of any damage to ground surface, trees, shrubbery, sidewalks & driveways. Eastside Paving, Inc. is not responsible for pavement failure due to unknown or defective subgrade. Any deviation from the work described above involving extra charges over the prices mentioned will only be executed upon written or verbal orders. All agreements, verbal and written are binding. By signing below I accept full responsibility for all cost necessary to collect all money owned associated with work performed including attorney fees. Permits not included unless stated in proposal.

Authorized Signature:

Sean Patrick, Estimator Cell#: 503-519-6479

Acceptance of Proposal – The above prices, specifications and conditions are satisfactory and are hereby accepted. You are authorized to do the work as specified. Payment to be made upon completion of work.

Date of Acceptance: _____ Signature____

| 71 # 74 | Donation and the second | Estimated Oversity | 11-2 | Unit Drice | Total Brice |
|-------------------|------------------------------|--------------------|-------------|----------------|-------------|
| Project Location: | Clackamas, OR | | Bid Date: | 10/8/2024 | |
| Project Name: | New Clackamas Village | | Bid Number: | Revision #3 | |
| <u> </u> | Lake Oswego, OR 97035 | | Fax: | | |
| Address: | 12572 Boones Ferry Rd | | Phone: | (503) 913-3383 | |
| То: | Asa Construction Corporation | | Contact: | Estimating | |

| Item # | Item Description | Estimated Quantity | Unit | Unit Price | Total Price |
|-----------|---|------------------------|--------|-------------|-------------|
| Added Wor | k | | | | |
| 1000 | East Rain Garden Planting (1,056sf) (Includes Soil, Plan Mulch And Splashpad/Berm) | nts, 1.000 | LS | \$12,200.00 | \$12,200.00 |
| 2000 | West Rain Gardan Planting (Added Area 654sf) | 1.000 | LS | \$7,550.00 | \$7,550.00 |
| 3000 | Added Trees | 10.000 | EACH | \$750.00 | \$7,500.00 |
| 4000 | 1 Year Of Maintenance For Added Scope | 1.000 | YEAR | \$9,000.00 | \$9,000.00 |
| | To | tal Price for above Ad | ded Wo | rk Items: | \$36,250.00 |

Total Bid Price: \$36,250.00

Notes:

- Excludes seperation layer and drain rock in Rain Gardens
- Excludes tree grates and frames if required
- Excludes fences, gates, any asphalt or concrete work
- Excludes clearing and grubbing
- Excludes excavation and sub grade preparation
- Price excludes any Area Preparation
- Excludes Traffic Control
- · Water to be provide on site by the General contractor
- Sediment fence price includes one mobilization, add \$1,000 for each additional mob
- We are an Oregon COBID Certified WBE/DBE #193
- The above prices do not include a bond, add 2.5% if bond is required.
- The above prices do not include Permits.
- The above prices are firm for acceptance within 30 days from the bid opening
- We are a non-union contractor and will not participate in union agreements
- We do not participate in any apprenticeship programs
- This quote is to become part of the sub-contract
- Insurance Certifications will be furnished. Additional Insurance specifications or requirements will be at the expense of Prime Contractor. General Liability General Aggregate \$2,000,000.00, BL&PD Combined \$1,000,000.00, Personal Injury \$1,000,000.00, Excess/Umbrella \$4,000,000.00.
- The above price is based on a mutually agreed upon schedule.

| ACCEPTED: The above prices, specifications and conditions are satisfactory and hereby accepted. | CONFIRMED: Anderson's Erosion Control Inc. |
|---|--|
| Buyer: | |
| Signature: | Authorized Signature: |
| Date of Acceptance: | Estimator: |

10/8/2024 8:00:45 AM Page 1 of 1

Toby Davis Concrete, Inc PO Box 9 Woodburn Or 97071

| Material for trash enclosure adds 2yds of concrete and 6 sticks of rebar. | \$ 478 |
|---|-------------------------|
| Labor for trash enclosure adds | \$ 1,053 |
| | |
| Material for 1,500 s.f of 6in fire lane W/ #4 rebar 18in o.c is 30 yds of consticks of rebar. | crete & 128 \$ 7,792 |
| Labor for 1,500 S.f of 6in fire lane. | \$ 9,258 |
| Labor to install removable Ballards. | \$ 900 |
| | |
| Sidewalk deduct | \$-11,376 |

Total: \$8,105.00

Toby Davis Concrete INC PO Box 9 Woodburn Or 97071

Bill To
ASA Construction
Clackamas Emergency Shelter CO 1

| Date | Invoice No. | P.O. Number | Terms | Project |
|----------|-------------|-------------|-------|---------|
| 11/12/24 | 254 | | | |

| Item | Description | Quantity | Rate | Amount |
|----------------------|---------------|----------|----------------------|------------------------|
| concrete concrete | Rebar Labor | | 2,290.00 1,471.50 | 2,290.00T 1,471.50T |
| | | | | |
| | | | | |
| Thank you for | your business | | Subtotal | \$3,761.50 |
| | | | | |
| | | | Sales Tax (0.0%) | \$0.0 |
| | | | Total | \$3,761.50 |



Title:_____

1802 NE 99th Street Vancouver, WA 98665 360-574-1022

Page 1

CONTRACT CHANGE ORDER

| Change Order #: Change Order Date: Job Number: | MOD1 11/6/2024 245669 | | | | |
|---|---|--|--|--|--|
| To: Toby Davis Concrete 450 Hermanson St Woodburn, OR 97071 | Project: New Clackamas Village CLACKAMAS COUNTY, OR | | | | |
| Original Contract Amount: \$6,189.00 Total Previous Change Orders: Total Before this Change Order: Amount of this Change Order: \$1,875.00 Revised Contract Amount: \$8,064.00 | \$0.00 \$6,189.00 | | | | |
| Change description: REVISED DRAWING SET DATED 08/15/2024 PER REVISED DRAWING SET, ADDED REINFORCING AT SLEEPING & BATH UNIT BATH UNIT FOOTING DEPTH AND STEM WALL HEIGHT REVISED | | | | | |
| SLEEPING UNIT INTERIOR STEM WALL & FOOTING NEWLY ADDED DETAILING/PM TIME | | | | | |
| Change pricing: 1,962 Lbs. \$1,87 | '5.00 | | | | |
| Please return a signed copy: | | | | | |
| Toby Davis Concrete | | | | | |
| Signed: | | | | | |
| Dated: | | | | | |



1802 NE 99th Street Vancouver, WA 98665 360-574-1022

Page 1

CONTRACT CHANGE ORDER

| MOD2 11/6/2024 245669 | | | | | | |
|--|--|--|--|--|--|--|
| Project: New Clackamas Village CLACKAMAS COUNTY, OR | | | | | | |
| \$0.00 \$6,189.00 | | | | | | |
| Change description: REVISED DRAWING SET DATED 08/15/2024 | | | | | | |
| PER REVISED DRAWING SET, ADDED REINFORCING @ KITCHEN & DINING UNIT FOOTING DEPTH & STEM WALL HEIGHTS REVISED MID SPAN FOOTING AND FOUNDATION ACCESS NEWLY ADDED DETAILING/PM TIME. | | | | | | |
| Change pricing: 190 Lbs. \$192.00 | | | | | | |
| Please return a signed copy: | | | | | | |
| | | | | | | |
| Signed: | | | | | | |
| Dated: | | | | | | |
| | | | | | | |



Change Order #:

1802 NE 99th Street Vancouver, WA 98665 360-574-1022

Page 1

CONTRACT CHANGE ORDER

MOD3

| Change Order Date: Job Number: | 11/6/2024 245669 | | | |
|--|---|--|--|--|
| To: Toby Davis Concrete 450 Hermanson St Woodburn, OR 97071 | Project: New Clackamas Village CLACKAMAS COUNTY, OR | | | |
| Original Contract Amount: \$6,189.00 Total Previous Change Orders: Total Before this Change Order: Amount of this Change Order: \$223.00 Revised Contract Amount: \$6,412.00 | \$0.00 \$6,189.00 | | | |
| Change description: REVISED DRAWING SET DATED 08/15/2024 PER REVISED DRAWING SET, ADDED REINFORCING @ OFFICE UNIT: FOOTING DEPTH & STEM WAL HEIGHT REVISED MID SPAN FOOTING & FOUNDATION ACCESS NEWLY ADDED DETAILING/PM TIME | | | | |
| Change pricing: 227 Lbs. \$223. | 00 | | | |
| Please return a signed copy: | | | | |
| Toby Davis Concrete | | | | |
| Signed: | | | | |
| Dated: | | | | |
| Title: | | | | |



ASA Construction 19100 S Hwy 99E Oregon City OR 97045 503-913-3383 asaconstruction.com

November 13, 2024

To whom it may concern,

Shortly after breaking ground on the Clackamas Emergency Shelter Project, it was brought to our attention that the driveway was not compliant with the fire marshal's ability to turn around a fire truck on the property in the case of an emergency. The architect had to redesign the asphalt driveway to create room for fire departments codes and change the elevation that the original drawings had called out which required additional excavation, rock and removal. In addition to the work required for the turnaround the client also added crawl space access in each building, added interior doors for safety, pathway bollards, additional square footage of the raingarden, additional trees, removable bollards, Knoxbox and supervision for ASA to oversee the additional work as described. ASA has worked closely with all our subcontractors to gather the best and most competitive pricing for the changes made in ASI 1. ASA Construction's total cost for this COR outside of subcontractors is \$77,493.90. This includes all additional hours for meetings, supervision, coordination with subcontractors, bond/insurance costs and ASA's overhead and profit markup. Additionally, ASA is requesting an extension of 48 days to the completion date, making the completion date March 24th, 2025. There was an almost three-month delay with getting the building permit issued which held up a large portion of the work starting.

Thank you,

Heather Asa, Owner
