## **OAK LODGE & GLADSTONE COMMUNITY PROJECT**

## Concord Task Force Meeting February 25, 2021





clackamas.us/community project

## **Project Overview**


- Schematic Design through Permitting
   Phases of work
- Schematic Design
- Public Involvement Plan
- Task Force Subcommittees
- Budget
- Near-term Schedule

## **OAK LODGE AND GLADSTONE COMMUNITY PROJECT**

OAK LODGE LIBRARY, COMMUNITY CENTER, PARK & NCPRD OFFICES



February 24, 2021

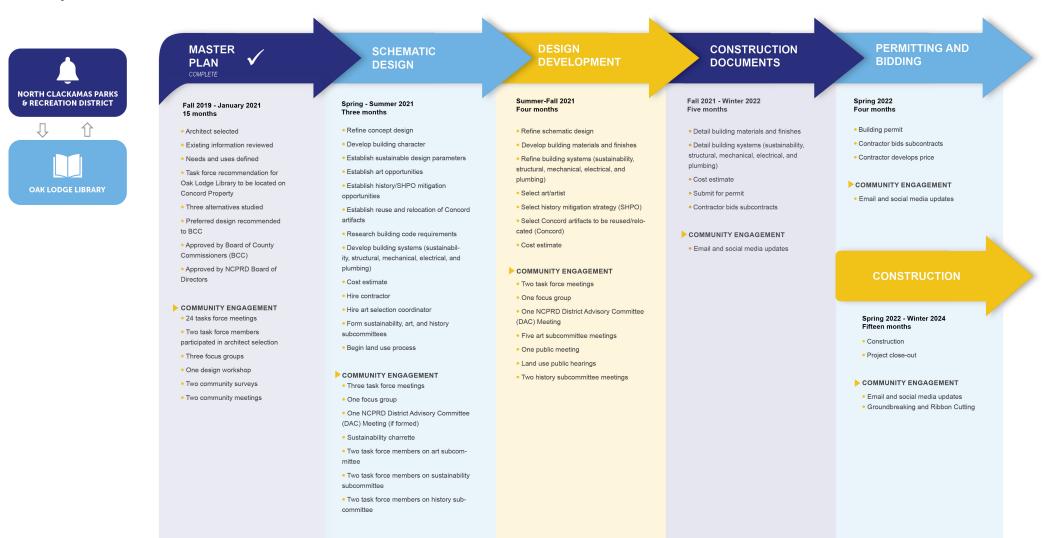

### MASTER PLAN COMPLETE

 $\mathbf{V}$ 

#### Fall 2019 - January 2021 15 months

- Architect selected
- Existing information reviewed
- Needs and uses defined
- Task force recommendation for
   Oak Lodge Library to be located on
   Concord Property
- Three alternatives studied
- Preferred design recommended to BCC
- Approved by Board of County Commissioners (BCC)
- Approved by NCPRD Board of Directors

### COMMUNITY ENGAGEMENT

- 24 tasks force meetings
- Two task force members participated in architect selection
- Three focus groups
- One design workshop
- Two community surveys
- Two community meetings

DESIGN

#### Spring - Summer 2021 Three months

- Refine concept design
- Develop building character
  - Establish sustainable design parameters

**SCHEMATIC** 

- Establish art opportunities
- Establish history/SHPO mitigation opportunities
- Establish reuse and relocation of Concord artifacts
- Research building code requirements
   Develop building systems (sustainabil-
- ity, structural, mechanical, electrical, and plumbing)
- Cost estimate
  Hire contractor
- Hire art selection coordinator
- Form sustainability, art, and history
- subcommittees
- Begin land use process
- COMMUNITY ENGAGEMENT
- Three task force meetings
- One focus group
- One NCPRD District Advisory Committee (DAC) Meeting (if formed)
- Sustainability charrette
- Two task force members on art subcommittee
- Two task force members on sustainability subcommittee
- Two task force members on history subcommittee

## 

DESIGN

Summer-Fall 2021 Four months

- Refine schematic design
- Develop building materials and finishes
- Refine building systems (sustainability, structural, mechanical, electrical, and plumbing)
- Select art/artist
- Select history mitigation strategy (SHPO)
- Select Concord artifacts to be reused/relocated (Concord)
- Cost estimate

#### COMMUNITY ENGAGEMENT

- Two task force meetings
- One focus group
- One NCPRD District Advisory Committee (DAC) Meeting
- Five art subcommittee meetings
- One public meeting
- Land use public hearings
- Two history subcommittee meetings

### CONSTRUCTION DOCUMENTS

### Fall 2021 - Winter 2022 Five months

- Detail building materials and finishes
- Detail building systems (sustainability, structural, mechanical, electrical, and plumbing)
- Cost estimate
- Submit for permit
- Contractor bids subcontracts

### COMMUNITY ENGAGEMENT

· Email and social media updates

### Spring 2022 Four months

- Building permit
- Contractor bids subcontracts
- Contractor develops price

#### **COMMUNITY ENGAGEMENT**

Email and social media updates

### CONSTRUCTION

#### Spring 2022 - Winter 2024 Fifteen months

- Construction
- Project close-out

#### COMMUNITY ENGAGEMENT

- Email and social media updates
- Groundbreaking and Ribbon Cutting



### SCHEMATIC DESIGN

### 

#### Spring - Summer 2021 Three months

### Refine concept design

- Develop building character
- Establish sustainable design parameters
- Establish art opportunities

• Establish history/SHPO mitigation opportunities

• Establish reuse and relocation of Concord artifacts

• Research building code requirements

 Develop building systems (sustainability, structural, mechanical, electrical, and plumbing)

- Cost estimate
- Hire contractor
- Hire art selection coordinator

• Form sustainability, art, and history subcommittees

Begin land use process

### COMMUNITY ENGAGEMENT

- Three task force meetings
- One focus group
- One NCPRD District Advisory Committee (DAC) Meeting (if formed)
- Sustainability charrette

• Two task force members on art subcommittee

• Two task force members on sustainability subcommittee

 Two task force members on history subcommittee

Summer-Fall 2021 Four months	Fall 20: Five m
Refine schematic design	• Detail
<ul> <li>Develop building materials and finishes</li> </ul>	• Detail
<ul> <li>Refine building systems (sustainability, structural, mechanical, electrical, and</li> </ul>	structuı plumbir
plumbing)	• Cost
<ul> <li>Select art/artist</li> </ul>	• Subm
<ul> <li>Select history mitigation strategy (SHPO)</li> </ul>	• Contr
<ul> <li>Select Concord artifacts to be reused/relo-</li> </ul>	
cated (Concord)	⊳сомм
Cost estimate	• Emai

### COMMUNITY ENGAGEMENT

- Two task force meetings
- One focus group

One NCPRD District Advisory Committee
(DAC) Meeting

- Five art subcommittee meetings
- One public meeting
- Land use public hearings
- Two history subcommittee meetings

# **Public Involvement Plan**

### Task Force Subcommittee

### **Public Meetings**

Goal: keep the community engaged and informed in the design process

- 2 Public Events (After SD & DD)
- 2 Underrepresented Focus Groups (After SD & DD) if feasible re: Covid
- 6 TF Meetings
- 2 Land Use Public Hearings
- 2 DAC Meetings

### **Sustainability**

Goal: Review and prioritize sustainable design strategies

- Sustainability Charette
   (workshop)
- 1.5% Green Energy Technology (GET)
- Work with Energy Trust of Oregon (ETO)
- Review potential ETO
   Incentives
- Report to Task Force

### Task Force Subcommittee

### Art

Goal: Review public art opportunities in the community park, community center/library and plaza

- 1% of Project Budget
   Dedicated to Art
- Coordinate with Friends
   of the Library
- Work with a public art facilitator
- Identify Opportunities/ Locations
- Select Artist
- Review Art progress
- Report to Task Force

### Task Force Subcommittee

### History

Goal: Review options for State Historic Preservation Office (SHPO) requirements and integration of artifacts from the existing building and interpretive displays, and integration of Oak Grove history


- Fact Finding/listening session. Review existing building artifacts
- Review of proposed SHPO mitigation strategies
- Provide input on
   interpretive display
- Report to Task Force

1 Meeting

**5-6 Meetings** 

**3** Meetings

## **Subcommittee Structure**

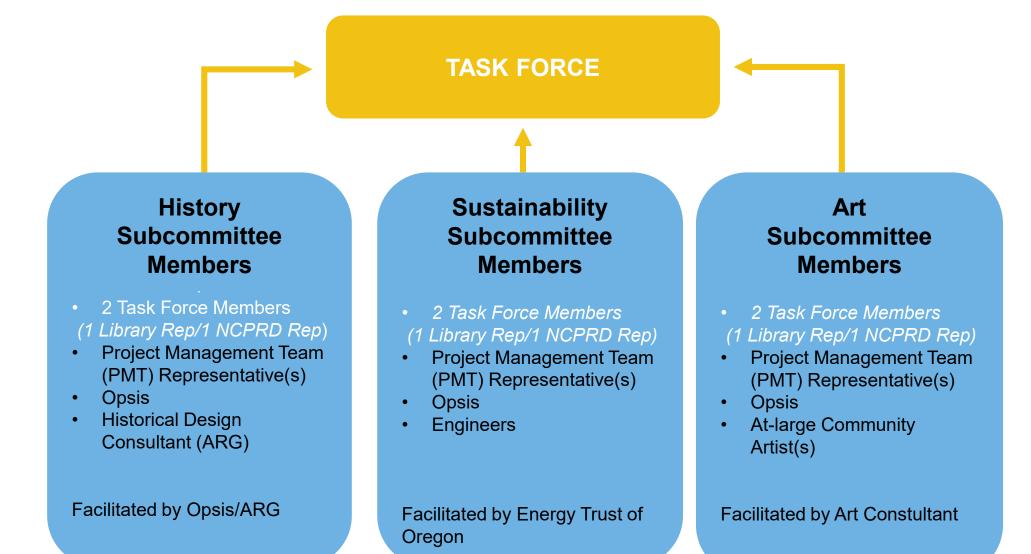

## **Q & A**

# **Cost Review**

## **Total Project Cost**

Total Project Cost is made up of Direct and Indirect Project Costs

## 1. Direct Project Costs:

Expenses directly related to construction

- Contractor materials, labor, insurance, profit, etc
- Demolition
- Earthwork
- Site Improvements
- Building
- Street and Sidewalk work

2. Indirect Project Costs:

Expenses NOT directly related to labor and physical building materials

- Survey
- Environmental work (removing oil tanks)
- Architectural and Engineering Fees
- Permits
- Testing and Inspections
- Community Engagement
- Project staff
- Construction Management

## **Oak Lodge Library Total Project Cost**

 Master Plan Total Project Cost
 \$12,100,000

 Direct Cost
 \$9,300,000

 Indirect Cost
 \$2,800,000

- Direct Cost by Cost Estimator
- Indirect Cost = 30% of Direct Cost Lump sum, place holder Industry standard for many projects




## **Oak Lodge Library Total Project Cost**

 Updated Total Project Cost
 \$14,000,000

 Direct Cost
 \$9,900,000


 Indirect Cost
 \$4,100,000

- Direct cost developed by a cost estimator
- Indirect cost is detailed estimate Includes five categories of work 40 unique costs

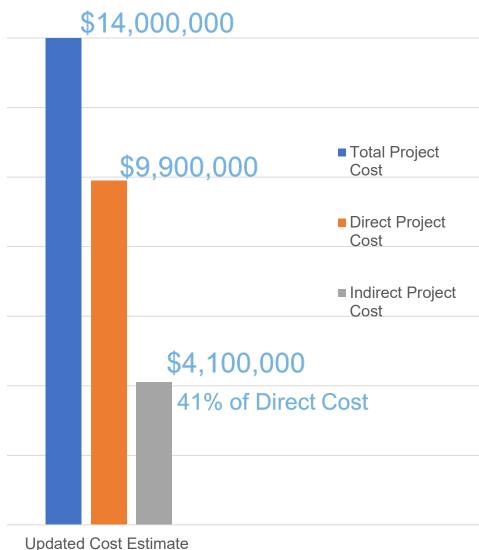

2/2021

## **Oak Lodge Library Total Project Cost**

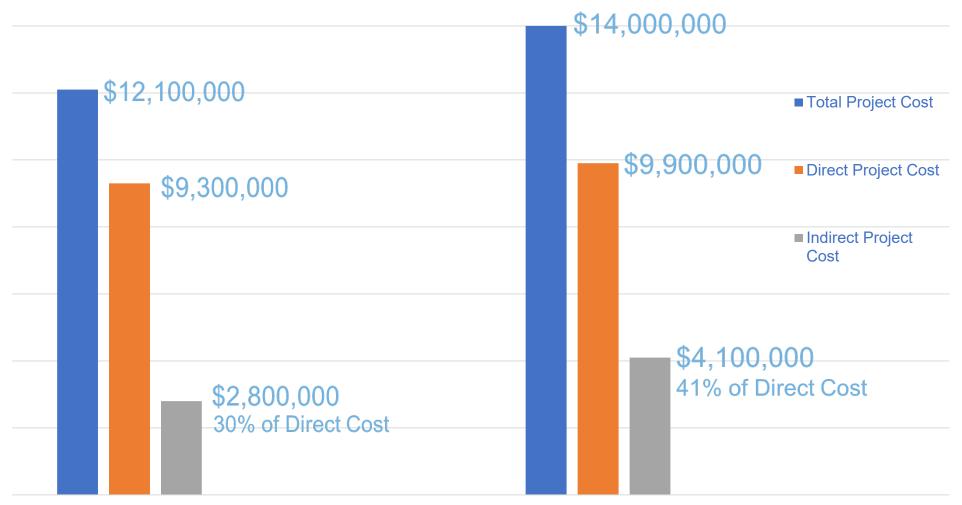

Master Plan Estimate 11/2020

Updated Cost Estimate 2/2021

## **NCPRD Total Project Cost**

 Master Plan Total Project Cost
 \$23,700,000

 Direct Cost
 \$18,200,000

 Indirect Cost
 \$5,500,000

- Direct Cost by Cost Estimator
- Indirect Cost = 30% of Direct Cost Lump sum, place holder Industry standard for many projects



Master Plan Estimate 11/2019

## **NCPRD Total Project Cost**


Updated Total Project Cost Direct Cost Indirect Cost

<u>\$24,200,000</u> \$17,500,000 \$6,700,000

- Direct cost developed by a cost estimator
- Indirect cost is detailed estimate Includes five categories of work 40 unique costs



## **NCPRD Total Project Cost**

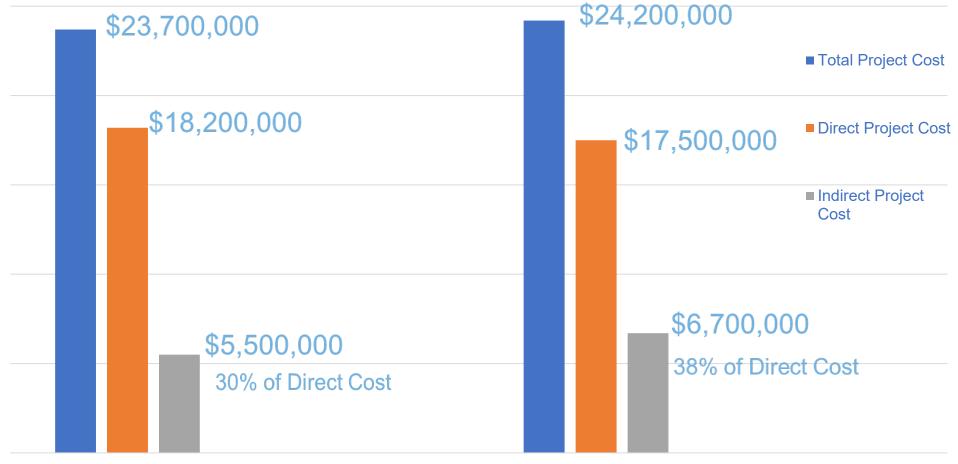

Master Plan Estimate 11/2020

Updated Cost Estimate 2/2021


# Library and NCPRD Total Project Cost Why the change?

- Indirect Cost
  - Lump sum, place holder vs. detailed, verified (to the extent possible)
- Detailed Indirect Project Cost Estimate has four categories:

#### **Property Building Professional Project Actuals** Support Related **Services** to-date Library Acquisition Arch. & Eng. Project Master Plan ٠ Furniture ٠ from NCPRD Public Fees Manager ٠ Equipment Acquisition of Public (Staff PM) Involvement Signage Olive Ave. Public Involvement PM Interim • • Security from Wal-Mart (Contract Building Meetings System and Brolin Permit PM) Staff ٠ Contractor Mailers System Dev. Charges Preconst. Owner's Rep. (SDCs) Art/Artist (Contract) ٠ Testing

## Oak Lodge Library and NCPRD Community Center, Offices, and Park

Project is a high priority for the County

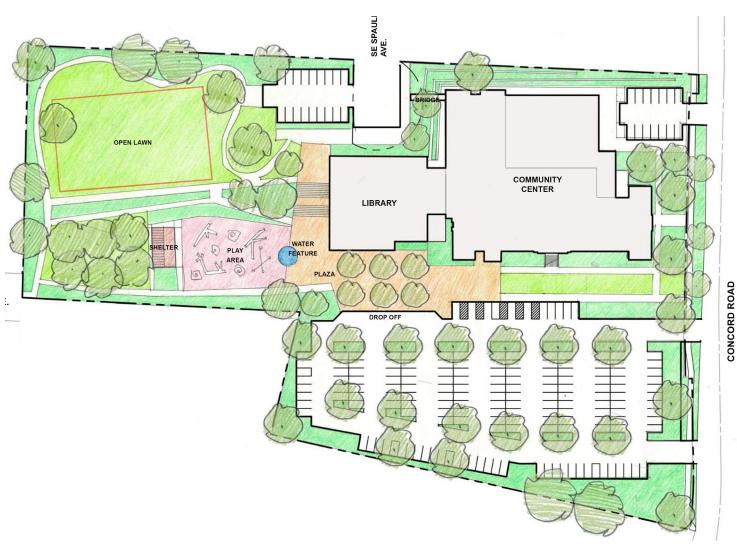

## **Q & A**

## Next Steps/Near-term Schedule

- BCC Policy Session March 9th Update
- BCC Business Meeting March 18<sup>th</sup> Approve Opsis Contract
- Next Task Force Meeting April 8<sup>th</sup> (tentative)
- Task Force Organization Future
  - Subcommittee members
  - Vote for Chair, Vice-chair (terms are up)
